

ARANSAS COUNTY ROAD & BRIDGE

PHONE: (361) 790-0152
EMAIL: roadbridge@aransascountry.org
1931 FM 2165, ROCKPORT, TX 78382

-----FOR OFFICE USE ONLY-----

DATE RECEIVED:
\$50 CASH/CHECK #:
RECEIPT #:
WORK ORDER #:
PERMIT #:

DRIVEWAY PERMIT

PROPERTY OWNER: _____ PHONE: _____

MAILING ADDRESS: _____ EMAIL: _____

CONTRACTOR: _____ PHONE: _____

EMAIL: _____ PREFERRED METHOD OF CONTACT: _____

PROPERTY ADDRESS: _____ PROPOSED WIDTH OF DRIVEWAY: _____

IS THIS AN EXTENSION OF AN EXISTING DRIVEWAY? YES NO EXTENSION LENGTH: _____

1. THE ONLY MATERIAL PERMITTED FOR USE AS CULVERTS ARE **REINFORCED CONCRETE PIPES** WITH A **MINIMUM DIAMETER OF FIFTEEN (15) INCHES**.

2. THE COUNTY WILL SET THE ELEVATION HUB FOR THE CULVERT AND, IF NECESSARY, DIG THE DRAINAGE DITCH. CULVERTS **MUST** BE INSTALLED TO THE CORRECT FLOW LINE. **CULVERTS INSTALLED INCORRECTLY WILL BE REMOVED AT OWNER/CONTRACTOR EXPENSE.**

3. DRIVEWAY MUST BE INSTALLED AT **LEAST FIVE (5) FT AWAY** FROM PROPERTY LINE.

4. DRIVEWAYS LARGER THAN **FIFTY (50) FEET IN LENGTH** REQUIRE **INSTALLATION OF A CLEAN-OUT BOX**. TOTAL LENGTH OF DRIVEWAY **MAY NOT EXTEND PAST 75% OF PROPERTY FRONTAGE**.

6. CONCRETE DRIVEWAYS **MUST INCLUDE A FOUR (4) FOOT WIDE EXPANSION JOINT** ABOVE THE CULVERT.

-----PLEASE REPORT FLOODING & ACCESS ISSUES TO 361-790-0152-----

OWNER MUST MARK DESIRED LOCATION OF DRIVEWAY USING STAKES, FLAGS, OR SPRAY PAINT.
HUB **WILL NOT** BE SET WITHOUT PROPER MARKERS.

IT IS THE RESPONSIBILITY OF THE OWNER/CONTRACTOR TO CONTACT 811 FOR LOCATES **48 HOURS PRIOR** TO HUB INSTALLATION.

PLEASE INITIAL

I, THE OWNER OR AUTHORIZED AGENT, VERIFY THAT I HAVE READ AND AGREE TO THE TERMS LISTED FOR DRIVEWAY & CULVERT INSTALLATION.

PLEASE USE THIS SPACE TO SKETCH PROPOSED DRIVEWAY LOCATION.

PRINTED NAME

OWNER/CONTRACTOR SIGNATURE

DATE

FINAL INSPECTION REQUIRED WITHIN 24 HOURS OF COMPLETION

HUB INSTALLATION DATE

COMPLETED BY

FINAL INSPECTION DATE

COMPLETED BY

NOTES:

DRIVEWAY INSTALLATION INSTRUCTIONS

OWNER MUST MARK DESIRED LOCATION OF DRIVEWAY USING STAKES, FLAGS, OR SPRAY PAINT.
HUB WILL NOT BE SET WITHOUT PROPER MARKERS.

1. INSTALL CULVERT PIPE
2. LAYER DESIRED FILL MATERIAL TO TOP OF CULVERT
3. ADD FOUR (4) INCHES OF COVER MATERIAL
4. PAVED DRIVEWAYS MUST HAVE A FOUR (4) FOOT WIDE EXPANSION JOINT ABOVE THE CULVERT

PERMIT FEE: \$50
CASH, CARD, OR CHECK
MADE PAYABLE TO ARANSAS COUNTY

**CULVERT MUST BE INSTALLED AT THE FLOW LINE
SET BY THE ELEVATION HUB,
FACING TOWARD THE FLOW OF WATER.**

FAILURE TO FOLLOW THESE INSTRUCTIONS MAY RESULT IN
FLOODING, STANDING WATER, AND OTHER DRAINAGE ISSUES.

**CULVERTS INSTALLED INCORRECTLY WILL BE REMOVED
AT OWNER/CONTRACTOR EXPENSE.**

ACCEPTED MATERIALS

CULVERT PIPE:


- REINFORCED CONCRETE ONLY
- FIFTEEN (15) INCHES DIAMETER MINIMUM
- DRIVEWAYS MUST BE AT LEAST
EIGHTEEN (18) FEET WIDE

FILL MATERIAL:

- DIRT
- GRAVEL
- **PLEASE DO NOT USE**
SUGAR SAND

COVER MATERIAL:

- DIRT
- CALICHE
- RECLAIMED ASPHALT
- LIMESTONE
- CRUSHED CONCRETE

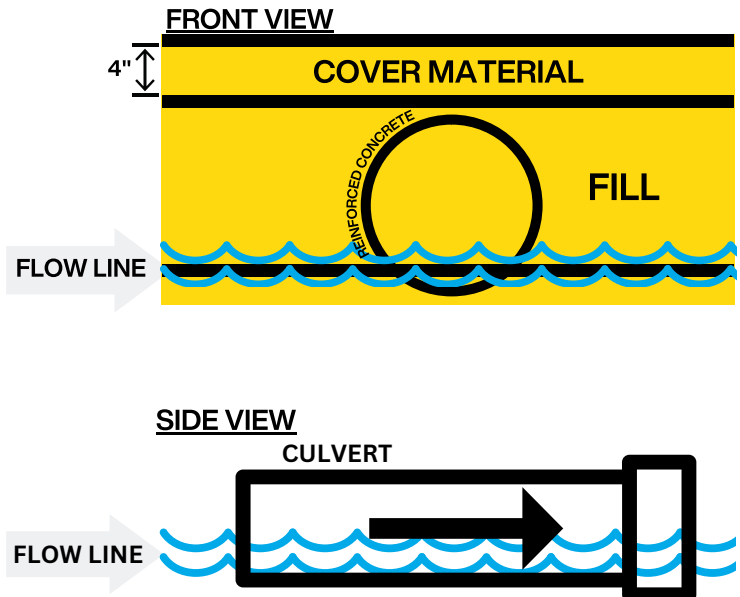

LOCAL CULVERT/DRIVEWAY CONTRACTORS

Burke Construction: 361-229-3493
Coastal Land Solutions: (361) 463-0032
Concrete Slabs, LLC: Pete Roel (361) 438-1037
Go With The Flow:
Richard Martin (361) 260-5052 & Donald Wagoner (361) 230-0227
Greg Boudreaux: (361) 230-1953
Long Nguyen: (361) 386-0048
Lamar Excavation: Mark Tardiff (361) 205-0114
Merrifield Sales & Service:
Gerald (806) 638-1088 & Shellie (806) 891-1085
Rocky Gudim: (361) 765-1506
Tidelands Piers & Bulkheads: (361) 935-8008
Please visit the City of Rockport's "Licensed Contractors" webpage for more information about local contractors.

NEED DIRT?

VISIT OUR FILL DIRT LOCATIONS!

- \$40 REFUNDABLE CASH DEPOSIT FOR KEY TO COUNTY FILL DIRT LOTS
- ACCESS FOR 2 WEEKS FROM DATE OF DEPOSIT
- RETURN THE KEY WITHIN 2 WEEKS, GET YOUR DEPOSIT BACK!

DIRT MAY CONTAIN METAL, GLASS, TRASH, ETC.

LOCATIONS:

1. S DOUGHTY & MURRAY EASEMENT
(LOCATED NEXT TO 503 S DOUGHTY)
2. 667 BANTY LANE
3. 331 RATTLESNAKE POINT ROAD
4. 221 S MESQUITE DRIVE
